First & Final Bill

M.A.R. 57 (Rule 116)

Measurement Book

No. C/09 189713

DOR ⇒ 02/03/2018

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency... M/s KRIDL .....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of the work: Improvements to Building and civil works at Mallasandra colony in Mallasandra ward no: 13 Sethhalli Subdivision						
	Estimate cost Rs: 30.00 Lakhs						
	JOB code No: 013-18-000045						
	AS No:→ EE/PD/AS/17/2017-18						
	TS No:→ CE/TS/268/2017-18						
	W.O.Nos→ EE/PD/W.O/08/2017-18 dated 4/12/2017						

Asst. Executive Engineer
Project Sub Division-I

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
							N

Index
- school Building
- Angarevadi
- Concrete pavement
- Kerb.

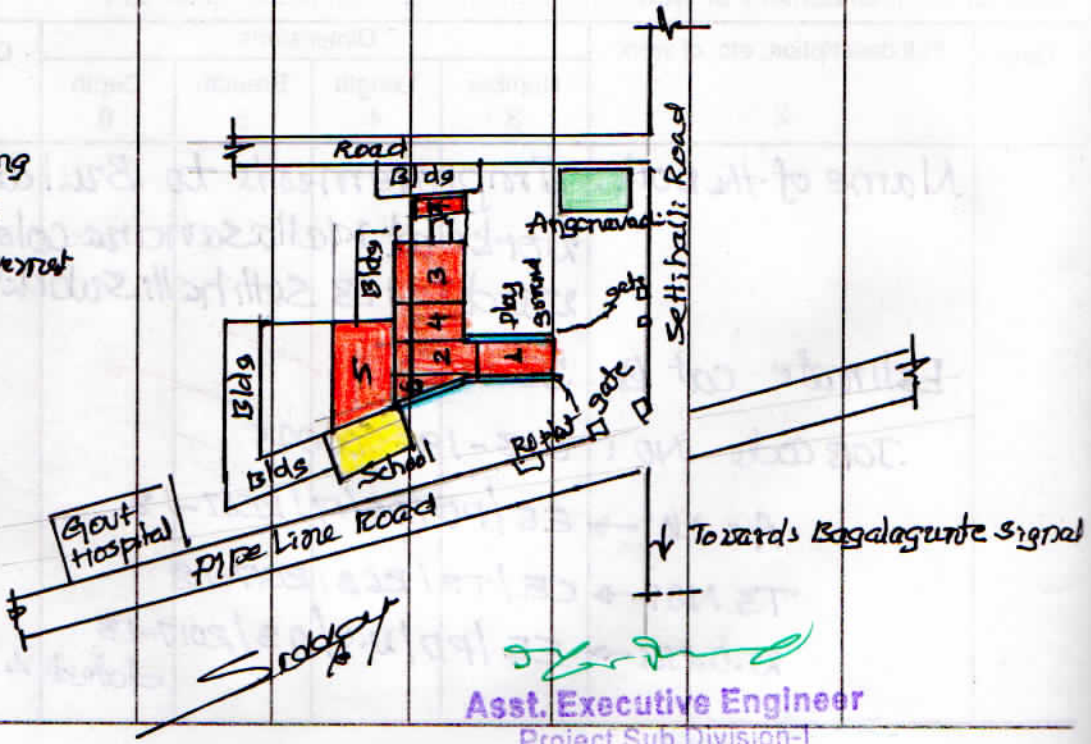

Asst. Executive Engineer
Project Sub Division-I
Dasarahalli Zone,

M.A.R. 57 (Rule 116)

Measurement Book

No. C/09 189714

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	1) Dismantling cement concrete flooring or plain cement concrete work including Removing conveying the debris to distance up to 200 mtr. (with an average thickness of 15cms) For School Building BF Pormeasurement Recorded in this MB vide page No: 189765 i.e 28.38 m^3 @ Rate Rs 59.40/m^3 Rs 1685=77						

Asst. Executive Engineer
Project Sub Division-I

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
2)	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220 kgs with 20mm and d/s granite metal coarse aggregate @ 0.84 cum and fine aggregates @ 0.56 cum machine mixed concrete laid in layers not exceeding 15cms thick well compacted etc complete						
	BF for measurement Recorded in this MB Vide page No: 189765						
	ie 23.76 m^3 @ Rate Rs 5449.68/-						Rs 129484=40
3)	Providing and laying in position reinforced cement concrete of design mix M-20 with OPC cement @ 300 kgs with 20mm & d/s graded granite metal coarse aggregates @ 0.64 cum and fine aggregates 0.43 cum machine mixed concrete laid in layers to be not exceeding 15cms thick well compacted etc complete						

Asst. Executive Engineer

M.A.R. 57 (Rule 116)

Measurement Book

No. C/09 189715

Serial No.....

Name of work.....From.....To.....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	BF For measurements Recorded in this MB Vide page No: 189766						
	i/e 30.33 M^3 @ Rate Rs 5985.36/-					Rs 181535-97	
4)	Providing and laying flooring using pre polished water cut/gang Saw 19mm thick granite laid over bed of 20mm thick 1:4 cm and jointed with neat cement slurry mixed with pigment to match shade of granite slab etc complete						

Asst. Executive Engineer

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Inside the school Building Hall -	1	18.70	5.30	—	99.11	
	Corridor	1	19.20	2.23	—	42.81	
	For skirting Inside	1	18.70	0.10	—	1.87	
	C & C	1	5.30	0.10	—	0.53	
		1	16.05	0.10	—	1.60	
		1	4.10	0.15	—	0.61	
		1	2.65	0.15	—	0.39	
	Corridor	2	19.20	0.10	—	3.84	
		2	2.23	0.10	—	0.44	
						151.20 m²	
			@ Rate	Rs 2826.52/m²		Rs 427672=22	

EXECUTIVE ENGINEER (Project)
Project Division
Bruhat Bangalore Mahanagara Palike,
Dasarahalli Zone, Bangalore-73.

Asst. Executive Engineer
